From specification to implementation

Sprint-by-sprint Jira tickets · 16 October 2026

01
Foundation

02
Detailed flows

03
Planned build

SPRINT 1 / CLOSED

Foundation, designed

15 Sep–2 Oct planned · completed 1 Oct

27

tickets in sprint

27

Done

Jira status ≠ independent acceptance or implementation audit.

SPRINT 1 / OUTCOME

Requirements before implementation


27 of 27 tickets marked Done; most outputs are plans and design artifacts.

Foundation	Git, AWS, Next.js/MapLibre and Supabase/PostGIS direction.
Access + data	User/profile schema, RLS policy drafts, RBAC and renter/landlord personas.
Experience + QA	Page wireframes, authentication workflow specifications and test plans.

SPRINT 1 / ARTIFACT SPOTLIGHT

SCRUM-64 · Design Landing Page Wireframe / Mockup

Ticket contents and artifact provenance

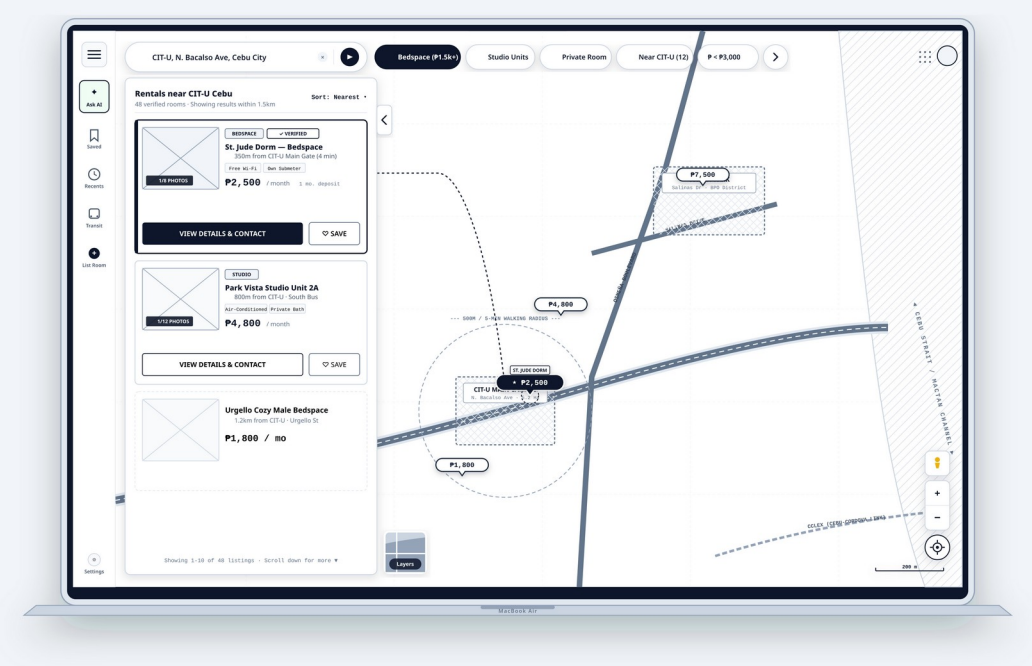

Desktop landing-page blueprint · wireframe, not a live application

DONE


- Map-led rental discovery layout
- Search, filters and listing preview are design concepts

Local wireframe; Jira lists same-named attachment

OPEN JIRA ISSUE

SCRUM-65 · Design Login Page Wireframe / Mockup

Ticket contents and artifact provenance

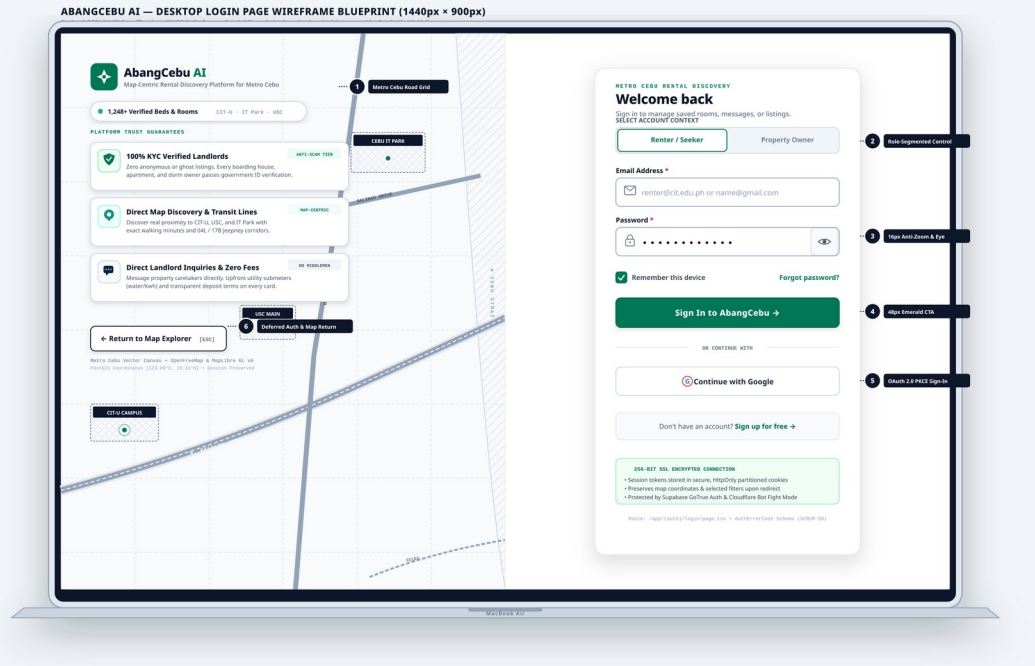

Desktop login-page blueprint · wireframe, not a live application

DONE

- Login page visual specification
- Auth implementation remains separate work

Local wireframe; Jira attachment linkage not independently checked

OPEN JIRA ISSUE

Sprint 1 · ticket register

1–6 of 27 / appendix page 1 of 5

SCRUM-10	Create AbangCebu System Flowcharts	DONE
SCRUM-49	Establish Git Branching & PR Collaboration Strategy	DONE
SCRUM-6	create AWS account for the team	DONE
SCRUM-55	Draft Row Level Security (RLS) Policy Specifications	DONE
SCRUM-62	Define Landlord Persona, Permissions & Capabilities	DONE
SCRUM-50	Configure UI Framework & Styling Guidelines	DONE

Sprint 1 · ticket register

7–12 of 27 / appendix page 2 of 5

SCRUM-51	Environment Variables & Secrets Governance Plan	DONE
SCRUM-52	Plan Supabase Project Structure & Extensions	DONE
SCRUM-53	Design Initial Database ERD Diagram	DONE
SCRUM-54	Define Users & Profiles Table Schema Specification	DONE
SCRUM-56	Specify User Registration Workflow & Data Contract	DONE
SCRUM-57	Specify User Login & Session Token Lifecycle	DONE

Sprint 1 · ticket register

13–18 of 27 / appendix page 3 of 5

SCRUM-58	Specify User Logout & Session Invalidation	DONE
SCRUM-60	Document Authentication Error Handling & Edge Cases	DONE
SCRUM-48	Plan Next.js 15 & MapLibre Project Foundation	DONE
SCRUM-64	Design Landing Page Wireframe / Mockup	DONE
SCRUM-63	Create Role-Based Access Control (RBAC) Matrix	DONE
SCRUM-61	Define Renter Persona, Permissions & Capabilities	DONE

Sprint 1 · ticket register

19–24 of 27 / appendix page 4 of 5

SCRUM-59	Specify Password Reset & Recovery Workflow	DONE
SCRUM-65	Design Login Page Wireframe / Mockup	DONE
SCRUM-66	Design Registration Page Wireframe / Mockup	DONE
SCRUM-67	Design User Dashboard Wireframe / Mockup	DONE
SCRUM-68	Design Profile Page Wireframe / Mockup	DONE
SCRUM-69	Draft Authentication Test Plan & Test Scenarios	DONE

Sprint 1 · ticket register

25–27 of 27 / appendix page 5 of 5

SCRUM-70	Draft Role & Access Permission Verification Test Cases	DONE
SCRUM-71	Draft Protected Route & Middleware Test Scenarios	DONE
SCRUM-72	Plan Authentication Baseline Latency & Load Strategy	DONE

SPRINT 2 / ACTIVE

Flows, specified

1–15 Oct planned · still active on 16 Oct

20

tickets in sprint

17

Done

3

In Development

Jira status ≠ independent acceptance or implementation audit.

SPRINT 2 / OUTCOME


Authentication and discovery mapped

17 Done; 3 In Development. The sprint still reads Active in Jira.

Authentication	Registration, login, reset, sign-out and failure flows; test matrices.
Spatial discovery	Map initialization, search, filters and pin/drawer interaction flowcharts.
Carry-over	SCRUM-125, SCRUM-126 and SCRUM-127 remain In Development.

SCRUM-104 · Sign Up Module & Flowchart: Registration & PKCE Verification

Ticket contents and artifact provenance

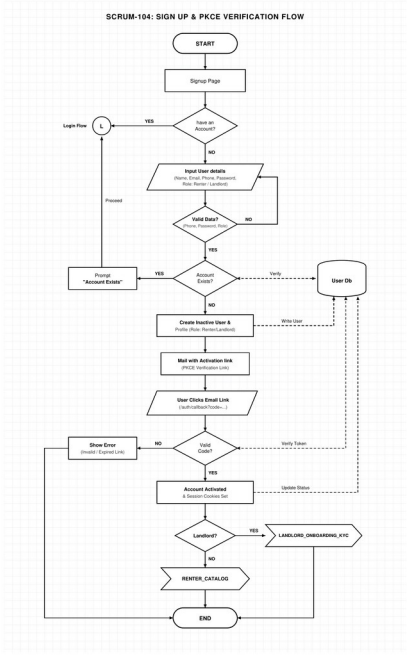

Registration + PKCE verification flow · diagram excerpt

DONE

- Defines registration, validation and duplicate checks
- Models email verification and PKCE callback


Local PNG; Jira lists matching editable .drawio attachment

OPEN JIRA ISSUE

SPRINT 2 / ARTIFACT SPOTLIGHT

SCRUM-116 · Landing Page Master Orchestration & Spatial Discovery Flowchart

Ticket contents and artifact provenance

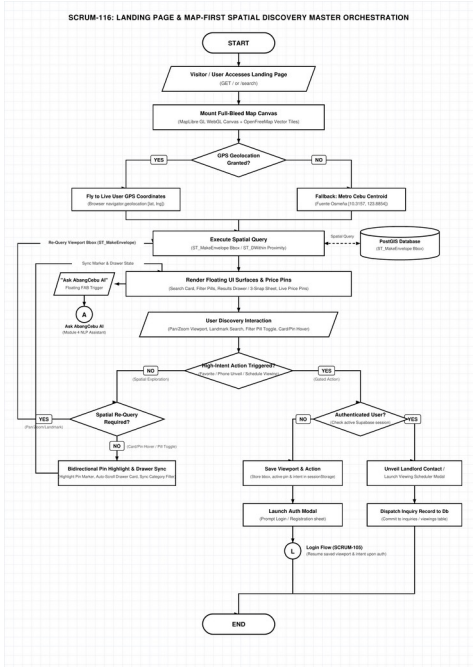

Map-first spatial discovery · diagram excerpt

DONE


- Map initialization and location choice
- Spatial query to price pins and results surfaces

Local flowchart; attachment linkage not independently checked

OPEN JIRA ISSUE

SCRUM-118 · Sub-Process 2.2: Spatial Search, Landmark Auto-Suggest & PostGIS Query Flowchart

Ticket contents and artifact provenance

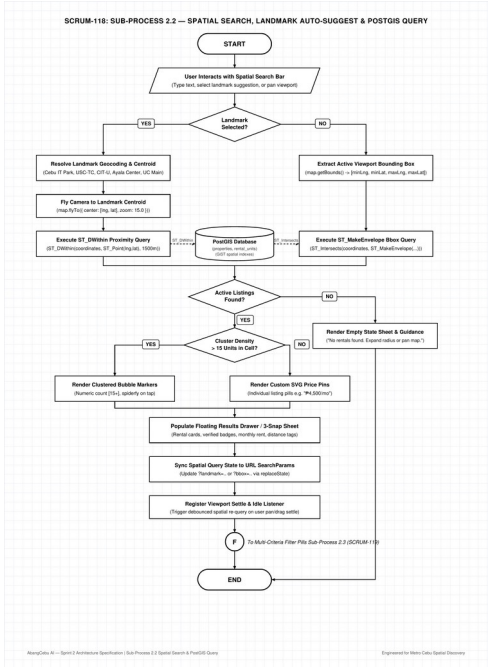

Spatial search query · diagram excerpt

DONE


- Landmark auto-suggest and viewport query
- PostGIS search specification, not implementation

Local PNG; Jira lists matching editable .drawio attachment

OPEN JIRA ISSUE

SCRUM-125 · Module 3: Landlord Onboarding & Listing Management Flowcharts

Ticket contents and artifact provenance

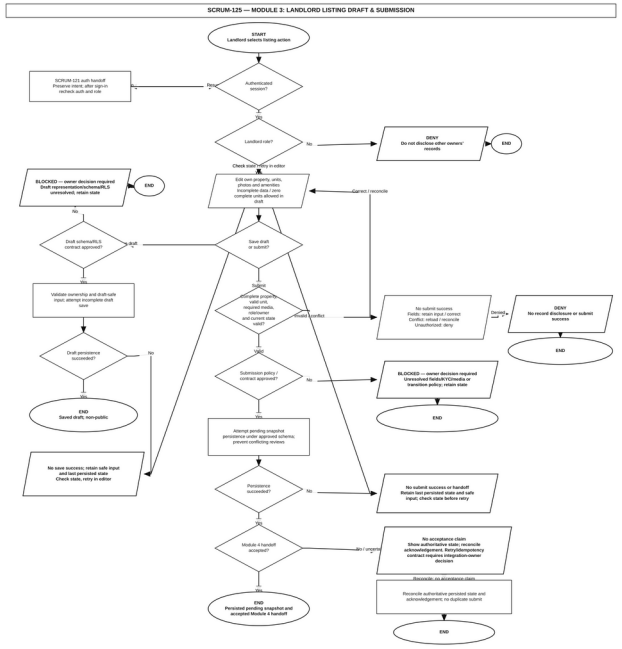

Landlord listing draft/submission · local draft

IN DEV

- Draft and submit listing flow
- Ticket remains In Development

Local draft; acceptance and Jira publication not verified

OPEN JIRA ISSUE

Sprint 2 · ticket register

1–6 of 20 / appendix page 1 of 4

SCRUM-104	Sign Up Module & Flowchart: Registration & PKCE Verification	DONE
SCRUM-105	Log In Module & Flowchart: Authentication & Session Token Lifecycle	DONE
SCRUM-106	Password Reset Module & Flowchart: Self-Service Recovery Workflow	DONE
SCRUM-107	Sign Out Module & Flowchart: Session Termination & Multi-Tab Sync	DONE
SCRUM-108	Error Handling & Suspension Module & Flowchart: Failure Taxonomy & UX States	DONE
SCRUM-109	Authentication Master Test Plan & Test Matrix	DONE

Sprint 2 · ticket register

7–12 of 20 / appendix page 2 of 4

SCRUM-110	Sign Up Module Test Plan & Registration Test Cases	DONE
SCRUM-111	Log In Module Test Plan & Session Token Test Cases	DONE
SCRUM-112	Password Reset & Sign Out Module Test Cases	DONE
SCRUM-113	Route Guards & Middleware Security Test Cases	DONE
SCRUM-114	Authentication Baseline Latency & Load Strategy	DONE
SCRUM-116	Landing Page Master Orchestration & Spatial Discovery Flowchart	DONE

Sprint 2 · ticket register

13–18 of 20 / appendix page 3 of 4

SCRUM-117	Sub-Process 2.1: Map Initialization, Viewport & Geolocation Flowchart	DONE
SCRUM-118	Sub-Process 2.2: Spatial Search, Landmark Auto-Suggest & PostGIS Query Flowchart	DONE
SCRUM-119	Sub-Process 2.3: Multi-Criteria Filter Pills & URL State Sync Flowchart	DONE
SCRUM-120	Sub-Process 2.4: Bidirectional Pin Marker & 3-Snap Gesture Drawer Flowchart	DONE
SCRUM-122	FUNCTION SPECIFICATION DOCUMENT FOR ABANG CEBU	DONE
SCRUM-125	Module 3: Landlord Onboarding & Listing Management Flowcharts	IN DEV

Sprint 2 · ticket register

19–20 of 20 / appendix page 4 of 4

SCRUM-126	Module 4: Admin KYC Verification & Listing Moderation Flowcharts	IN DEV
SCRUM-127	Module 5: Renter Favorites, Contact & Viewing Inquiry Flowcharts	IN DEV

SPRINT 3 / FUTURE

Build, then verify

No Jira start/end dates

35

tickets in sprint

35

Ready

Jira status ≠ independent acceptance or implementation audit.

SPRINT 3 / PLANNED WORK

Implementation has not started in Jira

35 tickets Ready; 0 Done. No Jira start or end date recorded.

Platform + data	EC2 staging, CI/CD, IAM, monitoring, migrations, RLS and PostGIS.
Application	Authentication, RBAC, shared UI, map search and listing interfaces.
Verification	Carry-over review, auth/RBAC QA, accessibility, load and system tests.

Sprint 3 · ticket register

1–6 of 35 / appendix page 1 of 6

SCRUM-134	Provision AWS EC2 staging environment for Next.js app	READY
SCRUM-135	Set up GitHub Actions CI pipeline (tsc, lint, build)	READY
SCRUM-136	Automate deployment from main to EC2 staging	READY
SCRUM-137	Define IAM least-privilege roles and policies for staging	READY
SCRUM-138	IAM access review and security audit of staging	READY
SCRUM-139	Set up monitoring, logging and uptime alerts for staging	READY

Sprint 3 · ticket register

7–12 of 35 / appendix page 2 of 6

SCRUM-140	Implement core listing tables migration	READY
SCRUM-141	Implement engagement tables migration (inquiries, saved_listings, reviews, audit_logs)	READY
SCRUM-142	Apply Row Level Security policies as migrations	READY
SCRUM-143	Create PostGIS search functions (viewport bbox and landmark radius)	READY
SCRUM-144	Seed Metro Cebu landmarks and sample listings	READY
SCRUM-145	Configure Supabase Storage buckets and database backups	READY

Sprint 3 · ticket register

13–18 of 35 / appendix page 3 of 6

SCRUM-146	Complete Database Specification workbook (.xlsx)	READY
SCRUM-147	Implement sign-up and email verification (PKCE)	READY
SCRUM-148	Implement login, session refresh and Remember Me	READY
SCRUM-149	Implement logout and multi-tab sign-out sync	READY
SCRUM-150	Implement password reset and recovery	READY
SCRUM-151	Implement RBAC middleware and route guards	READY

Sprint 3 · ticket register

19–24 of 35 / appendix page 4 of 6

SCRUM-152	Implement standard API error contract and auth error handling	READY
SCRUM-153	Build shared UI component library (Tailwind v4 tokens)	READY
SCRUM-154	Implement login, registration and password reset pages	READY
SCRUM-155	Implement MapLibre map canvas with Metro Cebu viewport and Locate Me	READY
SCRUM-156	Implement landing page, search bar and landmark auto-suggest	READY
SCRUM-157	Implement filter pills, URL state sync and results drawer	READY

Sprint 3 · ticket register

25–30 of 35 / appendix page 5 of 6

SCRUM-158	Module 6: AI Rental Assistant Flowcharts and Specification	READY
SCRUM-159	Define AI assistant API contract, prompt policy and evaluation set	READY
SCRUM-160	Extend Function Specification Document with Modules 3 to 5	READY
SCRUM-161	Review and close Sprint 2 carry-over (SCRUM-125, 126, 127)	READY
SCRUM-162	Execute authentication test plan against staging	READY
SCRUM-163	Execute RBAC and route guard tests	READY

Sprint 3 · ticket register

31–35 of 35 / appendix page 6 of 6

SCRUM-164	Browser, mobile and usability testing of auth pages and map UI	READY
SCRUM-165	Write test plans for Modules 3, 4 and 5	READY
SCRUM-166	Execute k6 load tests on staging (steady-state and burst)	READY
SCRUM-167	System test plan and first end-to-end run (auth to map to listing)	READY
SCRUM-168	Sprint 3 review, retrospective and reporting	READY

METHOD / SOURCE

How to read this deck

Snapshot: 16 Oct 2026 · board 1 · sprint IDs 4, 70, 72

All 82 issue keys appear once in the appendix and link to Jira.

The status labels are current Jira workflow states at snapshot time. They are not proof of code, tests, approval, or deployment. Visuals are local artifacts and are captioned with their verification limits.

Jira board: https://abangcebuai.atlassian.net/jira/software/projects/SCRUM/boards/1/backlog
